



Federal Government of Somalia

Somali Crisis Recovery Project (SCRP)  
Towards Recovery and Resilience Building in Somalia

CONTINGENCY EMERGENCY RESPONSE COMPONENT (CERC)



## Presentation Content

1. CERC Background, Objectives and implementing agencies
1. Progress as at today as per implementing agency
1. Disbursement Status
2. Safeguard and sustainability Consideration
1. Pending Tasks
2. Challenges and Lessons Learnt

# BACKGROUND

## CERC Objectives:

It seeks to tackle the spread of Covid-19 and limit its impact on the lives of the Somali population as well as on the economy and livelihoods.

The total allocated fund for CERC is \$20.5 million, spread across 8 activities, and is being implemented by either the government (FMoH and the PIU) or UN agencies (UNICEF, IOM and WHO).

# PROGRESS AS PER THE IMPLEMENTING AGENCY

## I. WHO

- : Purchase of PHEOC equipment for federal member states,
  - Expansion of community health workers reach across more districts.
  - RRTs deployed across many communities to conduct surveillance activities.
  - Procurement of laboratory equipment such as PCR machines and RNA extraction machines.
  - Procurement of interagency health kits (IEHKs)
  - Supporting a total of 24 technical specialists from all states to serve as technical advisors to their respective governments on technical aspects of the COVID-19 response in line with their fields of specialty, etc.

## ...SUMMARY OF PROGRESS MADE

### **2. UNICEF**

- So far, UNICEF made good progress towards the implementation of their activities through:
  - Commencement of RCCE activity implementation, further to review and approval of plans submitted by SMOHs, BRA, and FMOH.
  - Completed procurement of WASH supplies and procurement of hygiene kits.
  - Transportation of supplies to targeted state warehouse for distribution being completed before end of Dec 2021.

## ...SUMMARY OF PROGRESS MADE

### 3. IOM


- Like UNICEF, there have been delays in the process of disbursing funds to IOM's account brought upon by some technical impediments but that has since been rectified.
- IOM is implementing just \$871,500 worth of activities which is by far the least in all of CERC. Their progress is nearing its final stages. So far IOM has done the following:
  - Purchase of thermal scanners completed with plans to hand them over to three intended states (Hirshabelle, Jubbaland and Southwest).
  - Installation of thermal scanners and training of technical staff to operate and maintain them in the three mentioned states.
  - Shipment of oxygen plant to Galmudug state under way and construction of facility to house the plant already done.

# ...SUMMARY OF PROGRESS MADE

## 4. FGS

- While initially allocated just over \$2 million, an additional \$5 million was made to the FGS budget in February of this year as a result of the rising emergency cases during the second Covid wave.
- Though delays in implementation of FGS were caused by late recruitment of MoH SCRP staff as well as procurement processes and other impediments, so far the FGS has accomplished:
  - Recruited technical specialists at state level to be paid through CERC activities under WHO.
  - Responded to Covid-19 emergencies at hospitals throughout second and third waves by way of covering operation costs at main Covid-19 hospitals.
  - Made an agreement framework with an oxygen vendor to respond to rising deaths as a result of shortage of oxygen supply at martini hospital.
  - Is in the process of finalizing procurement of oxygen plants for two of the federal member states.
  - Rehabilitation of key storage facilities in FMS are underway
  - Is in the final stage of procuring key Covid-19 essentials such as medicines and PPEs

## Allocation per Implementing agency and Disbursement Allocation

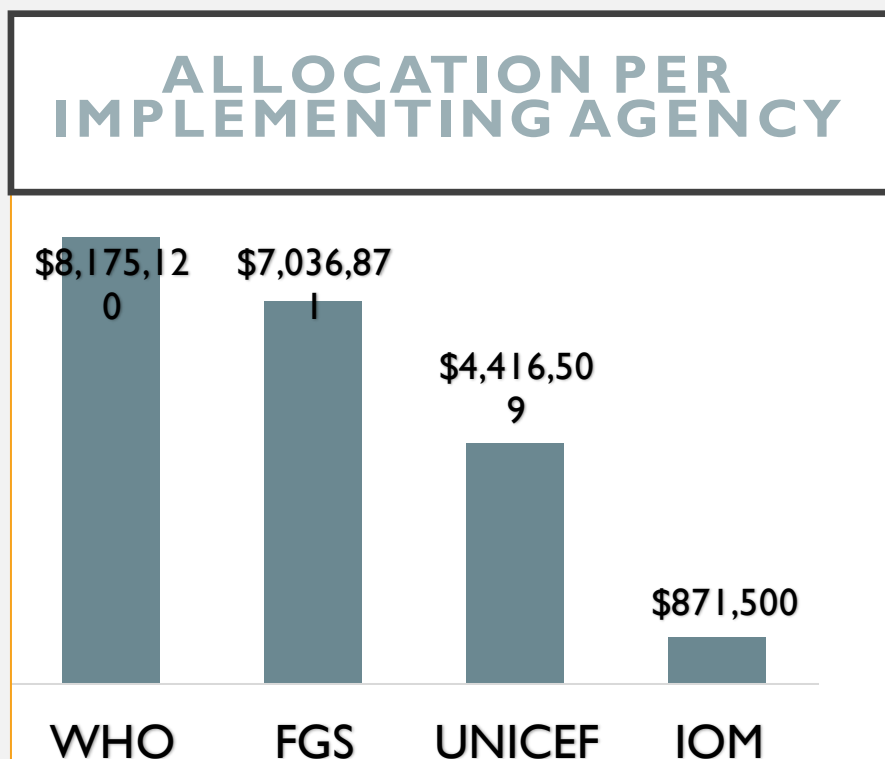

**TENTATIVE DISBURSEMENT STATUS**

Institutions	Allocation	PaidAmount	Balance	% Utilized
WHO	8,175,120.00	8,175,120.00	0.00	100%
UNICEF	4,416,508.86	4,416,508.86	0.00	100%
IOM	871,500.00	871,500.00	0.00	100%
FGS	7,036,871.14	861,977.10	6,174,894.04	12%
<b>Total Amount</b>	<b>20,500,000.0</b>	<b>\$ 14,325,105.96</b>	<b>\$ 6,174,894.04</b>	<b>70%</b>

N.B: MoF has completed the disbursement process of IOM and UNICEFF, the creation of commitment at the client-connection is remaining with the Bank


- ✓ FGS commitments: There are pending invoices of Oxygen supplies, locally made facemask and Hygiene supplies which almost totaling \$700,000 which we are expected to be paid early December 2021.



## UTILIZATION OF FUNDS PER IP AS OF NOV, 2021

Agency	Utilization of funds %
FGS	23%
WHO	64%
UNICEF	42%
IOM	68%

# PROJECT EXPECTED COMPLETION DATE(S) BY IP

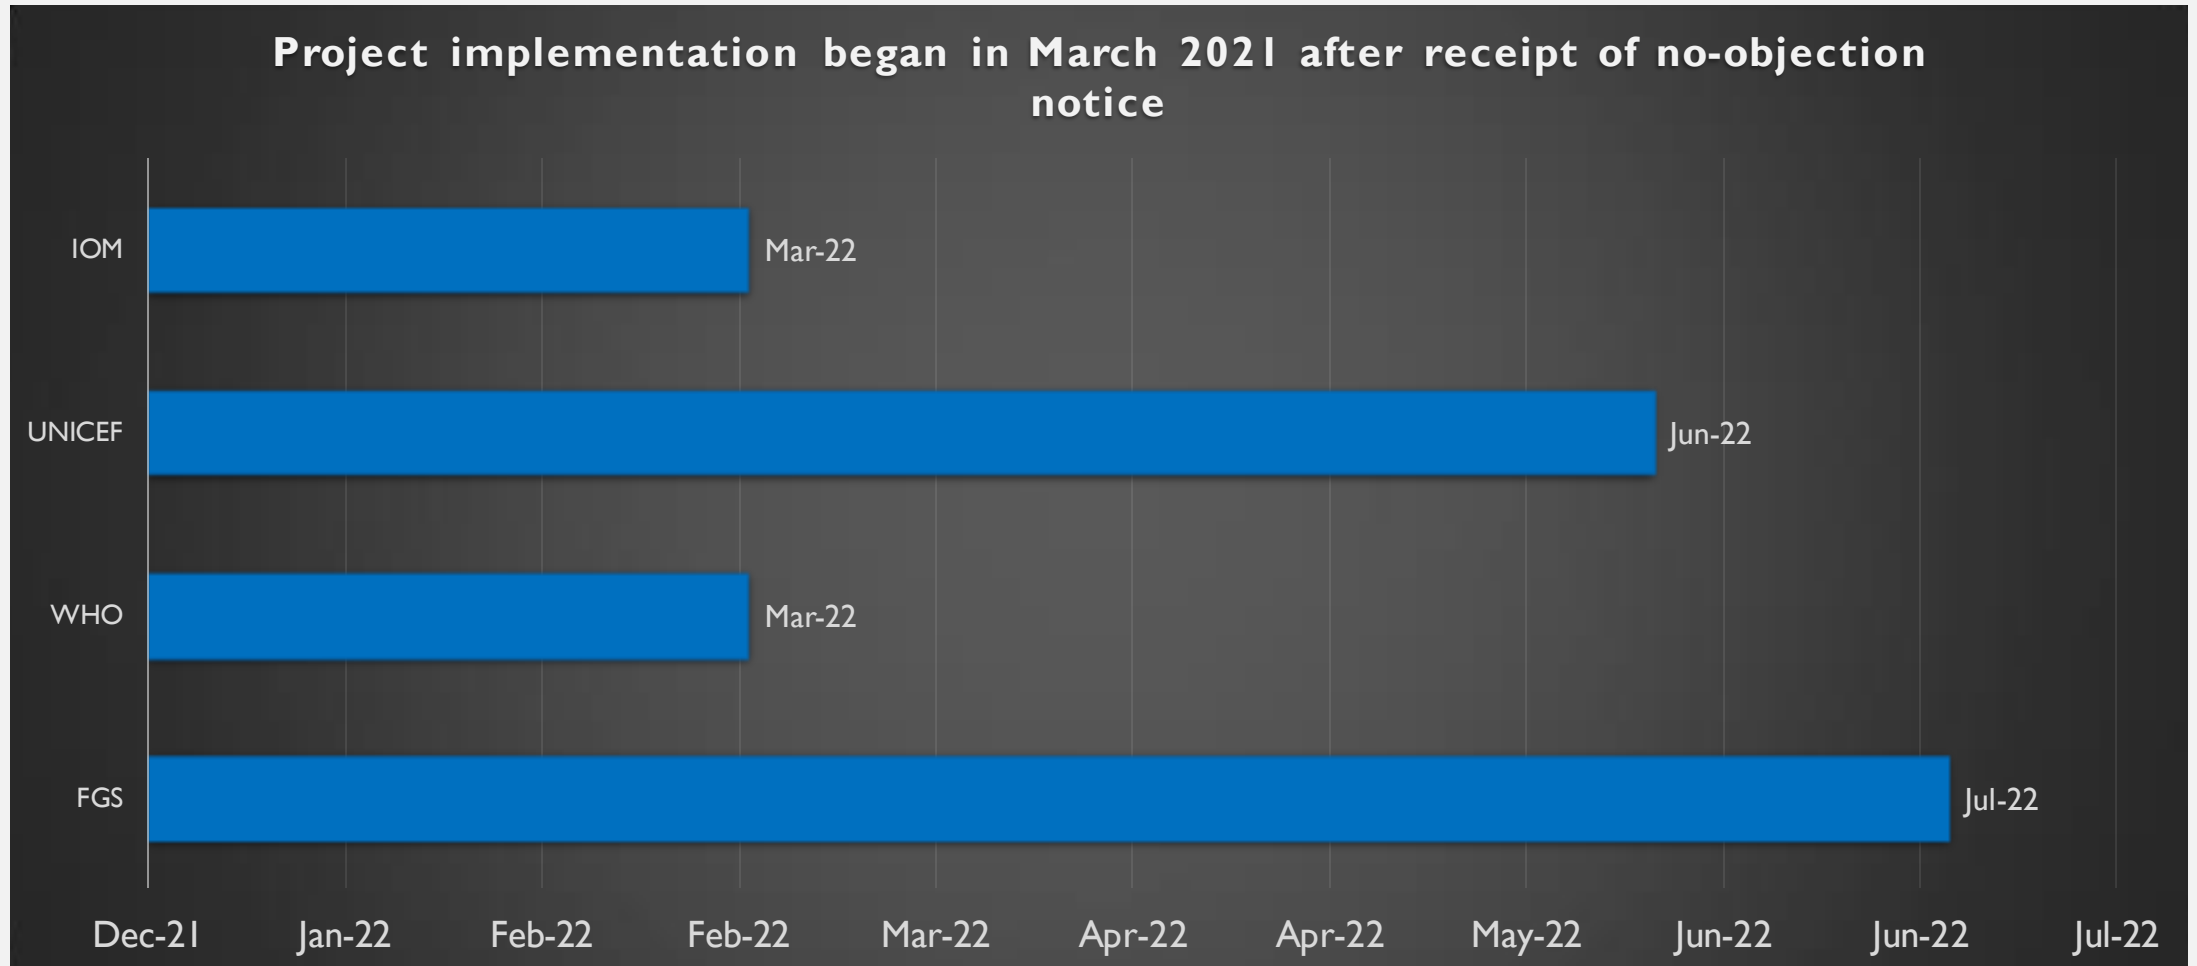

## CRITICAL CARE UNIT (CCU)

- The CCU is the 3<sup>rd</sup> component of SCRP that is meant to compliment progress made through CERC and is part of a greater effort to strengthen the institutional capacity and preparedness of governmental ministries agencies and departments to respond to various emergencies including health related ones.
- The health component in CCU is \$17 million that is spread across six activities to be implemented by the ministry of health and WHO.
- The primary aim of this component is to improve case management through strengthening the health sector's hospital and laboratory capacity.
- Over its three year plan, hospitals across the country will be equipped with both the supplies and human resource required to respond to both the short term and long-term effects of Covid-19 in Somalia.

# CRITICAL CARE UNIT

- In June 2021, after weeks of planning, we submitted a work-plan to the world bank detailing our objectives for strengthening the health system's response to Covid-19.
- Though preliminary reviews and assessments were conducted by the world bank, we still do not have the no-objection to begin implementation of CCU.

## KEY CHALLENGES

- Late recruitment of Project staff (Coordinator, Advisor, financial specialist, and communications) – **Late March 2021**.
- **No direct communication** between FMOH and the WB regarding implementation of the project. The project PIU is in MoF causing delays in executing emergency procurement of products and services
- Lack of separate procurement processes for emergency activities—both at the Ministry of Health, Ministry of Finance—**ONLY ONE PROCUREMENT SOPs**.

## NEXT STEPS

- No cost extension (NCE) request and discussions (ongoing)
- Discussions with the WB and MOF regarding modalities for fast-tracking CERC activities (now in process)
- Documentation on Lessons Learned and best practices
- Discussions on linkages with DAMAL CAAFIMAAD and COVID EMERGENCY VACCINES AND VACCINATIONS.
- Initiate FEDERAL MEMBER STATES discussions on CCU implementation.
